


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Wed 05/25/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:64°F Clear



Wind: 5 MPH S

Precipitation: .0"

Humidity: 79%

12:00 PM:80°F Partly Cloudy



Wind: 9 MPH S

Precipitation: .0"

Humidity: 56%

4:00 PM:88°F Mostly Cloudy



Wind: 13 MPH S

Precipitation: .0"




Humidity: 48%

Work Logs

Name	Description	Quantity	Hours
A Team Logic IT	Install Data & Voice wiring	1	8.0
Arc Electric	Install Feeder Cables to Transfer Switch. Electrical Work	2	8.0
Classic Touch Painting	Prep, prime, & paint, Walls Hollow metal Frames. Stain Wood Beams at Main Entrance Lobby.	3	8.0
Dumex Construction	Install Hanger wire for Ceiling Grid. Taper - Continues, Coating, sanding,	2	8.0
Heartland Cabinetry	Install Wood Trim	1	8.0
Midwest Mechanical	Install HVAC Duct work	2	8.0
Quinlan Security	Install Fire Alarm Wiring	1	8.0
Troop Contracting	Job Site Supervision. OAC Meeting	1	11.0
Total		13	107.0

Notes, Issues, Concerns


1. Transfer Switch Work

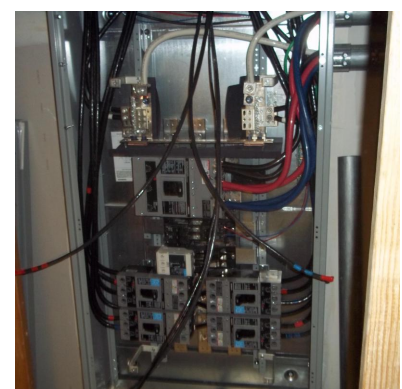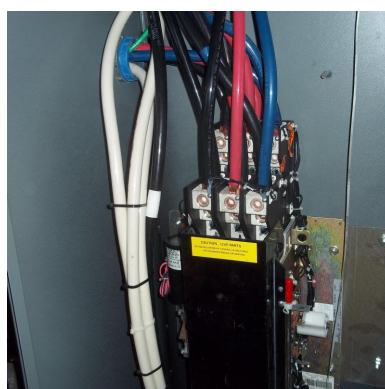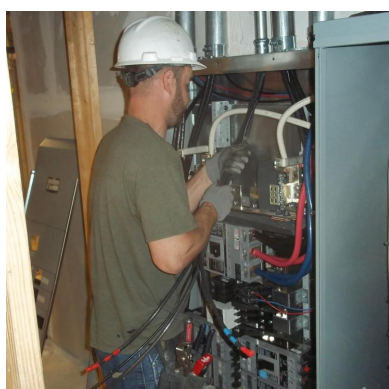


2. Voice & Data Wiring



3. Prep, Prime, Paint & Stain

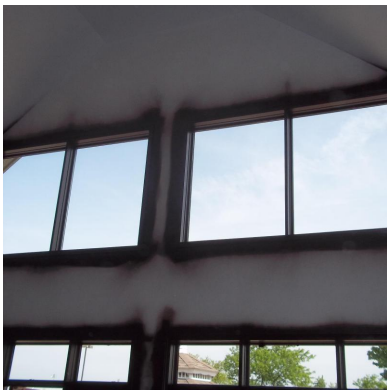


4. Wood Trim Install

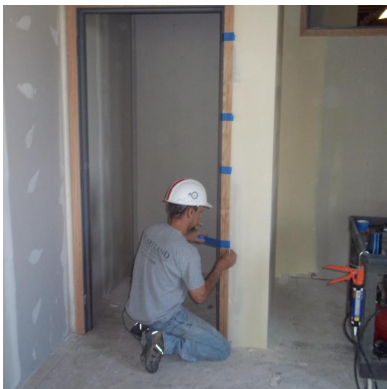

5. HVAC Duct Work



6. Drywall Taping

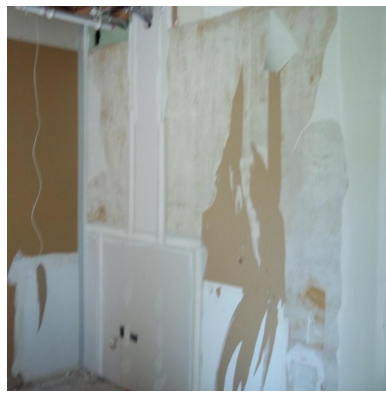

7. Preview Of Millwork



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	☒	☐	N/A
Hot issues that may effect schedule?	☐	☒	SIPS Panel System - Water Leak
Did weather cause any delays?	☒	☐	N/A
Any visitors on site?	☐	☒	OAC Weekly Meeting
Any areas that can't be worked on?	☐	☒	Board room & Community Rooms - SIPS Panel Roof
Any equipment rented on site?	☐	☒	Pole Braces to support Precast floor - Scissors Lift Painting Contractor



I, Dave Bender, verify this report is accurate and complete.
