


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Tue 05/31/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:66°F Partly Cloudy



Wind: 4 MPH NE
Precipitation: .0"
Humidity: 73%

12:00 PM:80°F Light Rain



Wind: 7 MPH SE
Precipitation: .01"
Humidity: 47%

4:00 PM:84°F Light Rain





Wind: 9 MPH SE
Precipitation: .01"
Humidity: 47%

Work Logs




Name	Description	Quantity	Hours
Arc Electric	Electricail Work	2	8.0
Classic Touch Painting	Prep, Prime, & Paint	3	8.0
Dumex Construction	2 - Carpenters, 1- Drywall Taper. Misc Drywall Install, Install Ceiling Grid, & Drywall Taping.	3	8.0
Heartland Cabinetry	Install Wood Casing on Hollow Metal Frames.	2	8.0
Midwest Mechanical	Install HVAC Duct Work	2	8.0
Troop Contracting	Job Site Supervision	1	8.0
Valley Fire Protection	Re- Install Fire Suppression @ Board Room	2	6.0
Total		15	116.0

Notes, Issues, Concerns


1. Ceiling Grid Install

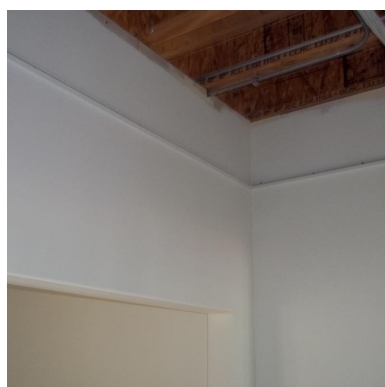

2. HVAC Duct Work

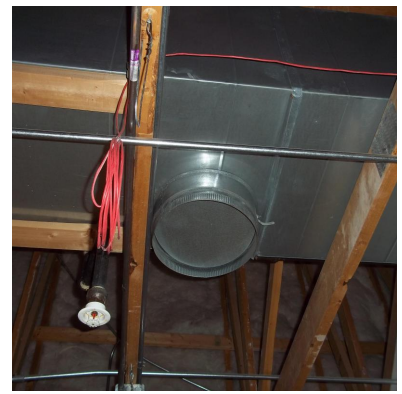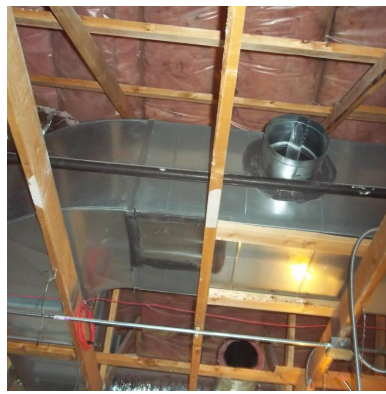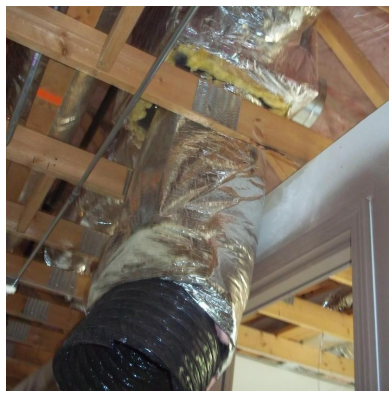


3. Prep, Prime, & Painting.

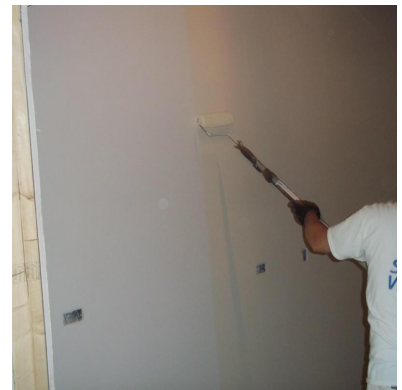

4. Fire Sprinkler - Reinstalled



5. Wood Casing Install

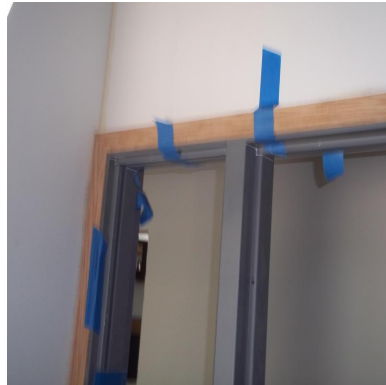

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	☒	☐	N/A
Hot issues that may effect schedule?	☐	☒	SIPS Panel System - Water Leak
Did weather cause any delays?	☒	☐	N/A
Any visitors on site?	☒	☐	N/A
Any areas that can't be worked on?	☐	☒	Board room & Community Rooms - SIPS Panel Roof
Any equipment rented on site?	☐	☒	Pole Braces to support Precast floor - Scissors Lift Painting Contractor



I, Dave Bender, verify this report is accurate and complete.
