


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Tue 06/21/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:63°F Clear



Wind: 3 MPH NW
Precipitation: .0"
Humidity: 75%

12:00 PM:78°F Clear



Wind: 8 MPH W
Precipitation: .0"
Humidity: 39%

4:00 PM:87°F Clear





Wind: 11 MPH W
Precipitation: .0"
Humidity: 32%

Work Logs


Name	Description	Quantity	Hours
Arc Electric	Electric Work	1	8.0
Classic Touch Painting	Painting	1	8.0
Dumex Construction	1-Ceiling Grid install. 1- Door Hardware 2- FRP 1- Drywall Taping	5	8.0
F & G Roofing	Shingle Install - SIPS Roof Repair	2	8.0
Heartland Cabinetry	Trim - Install	1	8.0
Premier Mechanical	HVAC Equipment Service Work	2	8.0
Superior Flooring	1- Carpet Install. 1- Ceramic Tile	2	8.0
Superior Labor	General Labor	1	8.0
Team Logic IT	Phone & Data Work	1	8.0
Troop Contracting	Job Site Supervision	1	10.0
Total		17	138.0

Notes, Issues, Concerns

1. Roof repair

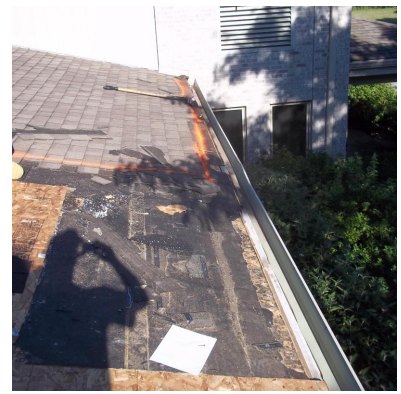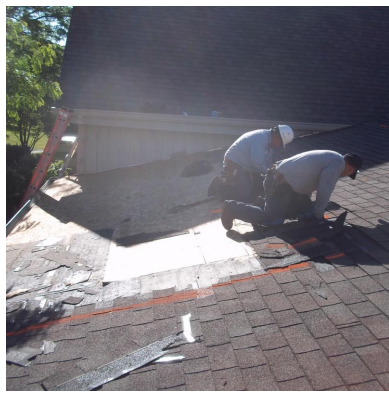

2. Ceramic Tile install Start

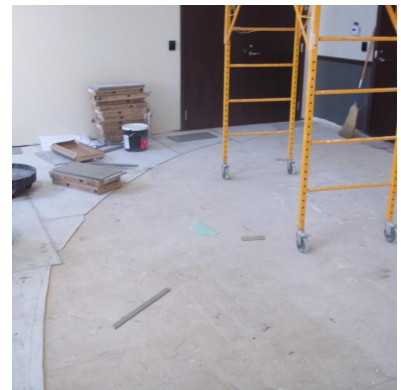

3. Wood Trim



4. Ceiling Hatch



5. SIPS Repair



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	☒	☐	N/A
Hot issues that may effect schedule?	☒	☐	N/A
Did weather cause any delays?	☒	☐	N/A
Any visitors on site?	☒	☐	N/A
Any areas that can't be worked on?	☒	☐	N/A
Any equipment rented on site?	☐	☒	Pole Braces to support Precast floor

A handwritten signature in black ink, appearing to read "DB", with a horizontal line extending to the right.

I, Dave Bender, have reviewed and completed this report.
