


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Mon 06/27/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:69°F Clear



Wind: 4 MPH SW
Precipitation: .0"
Humidity: 85%

12:00 PM:86°F Clear



Wind: 11 MPH W
Precipitation: .0"
Humidity: 51%

4:00 PM:90°F Clear



Wind: 15 MPH W
Precipitation: .0"
Humidity: 38%

Work Logs

Name	Description	Quantity	Hours
Arc Electric	Install New exit Signs, Install New Base Board Heaters,	1	8.0
Classic Touch Painting	Paint Hand railings, Touch Ups & Ceiling In Community Room	1	8.0
Dumex Construction	Drywall Install Board & Community Room, Install Ceiling Grid Community Room Kitchen.	3	8.0
e.Norman Security	Installation Of Security System	2	8.0
H & P Brick Work	Re- Install Brick Knee wall, SIPS Repair, & Infill work.	3	4.0
Heartland Cabinetry	Wood Trim Install, Material For Steel Column Wraps Delivered to Job.	2	8.0
Pace Systems	Install Video Monitors In Conference Rooms & Mayor's Office	2	8.0
Quinlan Security	Survey All Existing Fire Alarm Devices, Replace Defective Devices.	1	4.0
Superior Flooring	Cut Radius in ceramic Floor Tile Entrance Lobby, Install Wall tile infill Men's Public Washroom.	1	8.0
Superior Labor	General Job site Labor / Clean up, Move Material to Basement.	1	8.0
Troop Contracting	Job Site Supervision.	1	10.0
Total		18	130.0

Notes, Issues, Concerns

1. Radius Cut In Ceramic Tile




2. Exterior Brick Re- Install




3. Drywall Install Board Room



4. Video Monitors Installed

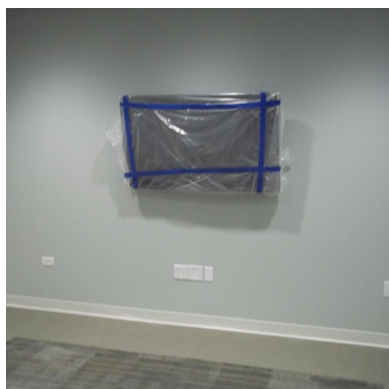

5. Baseboard Heaters Installed

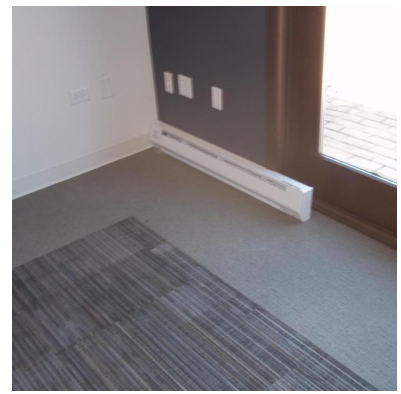

6. Material For Steel Column Wrap



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	☒	☐	N/A
Hot issues that may effect schedule?	☒	☐	N/A
Did weather cause any delays?	☒	☐	N/A
Any visitors on site?	☐	☒	Water Proof Basement Foundation Walls - 3.0 Hrs
Any areas that can't be worked on?	☒	☐	N/A
Any equipment rented on site?	☐	☒	Pole Braces to support Precast floor



I, Dave Bender, have reviewed and completed this report.
